


PHASE 3B (AUGUST 2018 - OCTOBER 2018) 1" = 160'-0"

92ND AVE. W

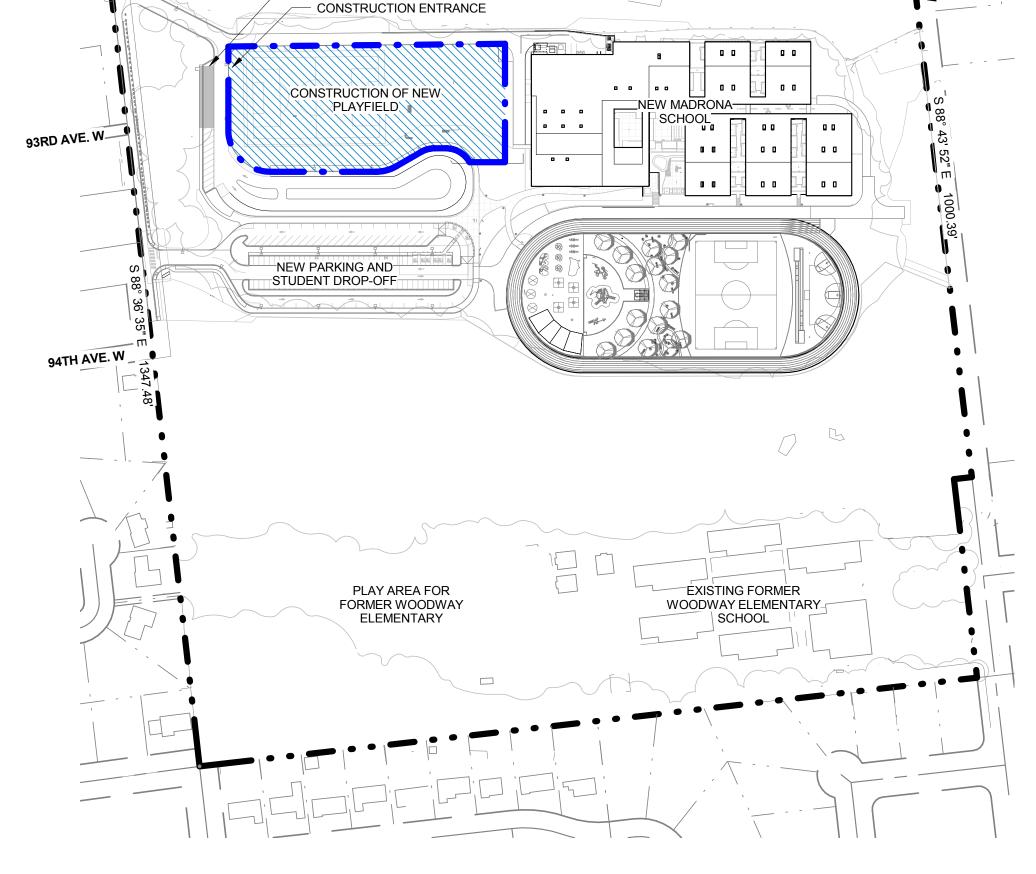

- CONTRACTOR PARKING

- DEMOLITION OF EXISTING TECH ROOM - UTILITY WORK AND CONSTRUCTION OF ATB DRIVE AT EAST ACCESS ROAD - EARTHWORK AND GRADING, BUILD NEW MADRONA SCHOOL PHASE 2 28 AUGUST 2017 - 24 JUNE 2018 - CONSTRUCTION ENTRANCE AT EAST ACCESS ROAD

GENERAL

- CONTRACTOR PARKING AT NORTH TRACK AREA, STAGING/STORAGE ON SOUTH TRACK AREA - BUILD NEW MADRONA SCHOOL - TEMPORARY FENCED PLAY AREA TO NORTH OF EXISTING SCHOOL

- TEMPORARY FENCED PLAY AREA TO NORTH OF EXISTING SCHOOL

- CONTRACTOR TO MAINTAIN EMERGENCY EGRESS FROM EXISTING BUILDINGS.

- PHASE 3A 25 JUNE 2018 AUGUST 2018
- COMPLETE NEW MADRONA SCHOOL
- CONSTRUCTION OF NEW TRACK AND PLAY STRUCTURES
- DEMO EXISTING MADRONA BUIDLINGS - PAVE STUDENT DROPOFF/PARENT PARKING

PHASING NOTES

- PRELIMINARY EARTHWORK AND GRADING

- CONSTRUCTION ENTRANCE AT EAST ACCESS ROAD

PHASE 1B 25 JUNE 2017 - 27 AUGUST 2017 - CONSTRUCTION ENTRANCE AT EXISTING SERVICE YARD

PHASE 1A 1 MAY 2017 - 25 JUNE 2017

- BUILD NEW MADRONA SCHOOL

- PAVE BUS LOOP
- PHASE 3B JUNE 2018-OCTOBER 2018 - COMPLETE CONSTRUCTION OF NEW PLAYFIELD

PHASING LEGEND



CONTRACTOR ACCESS

EXISTING BUILDING TO REMAIN DURING PHASE



EXISTING BUILDING

DEMOLISHED DURING PHASE

